


FUTURMAT F3 Pre installation Guide



15 Amp single phase male plug

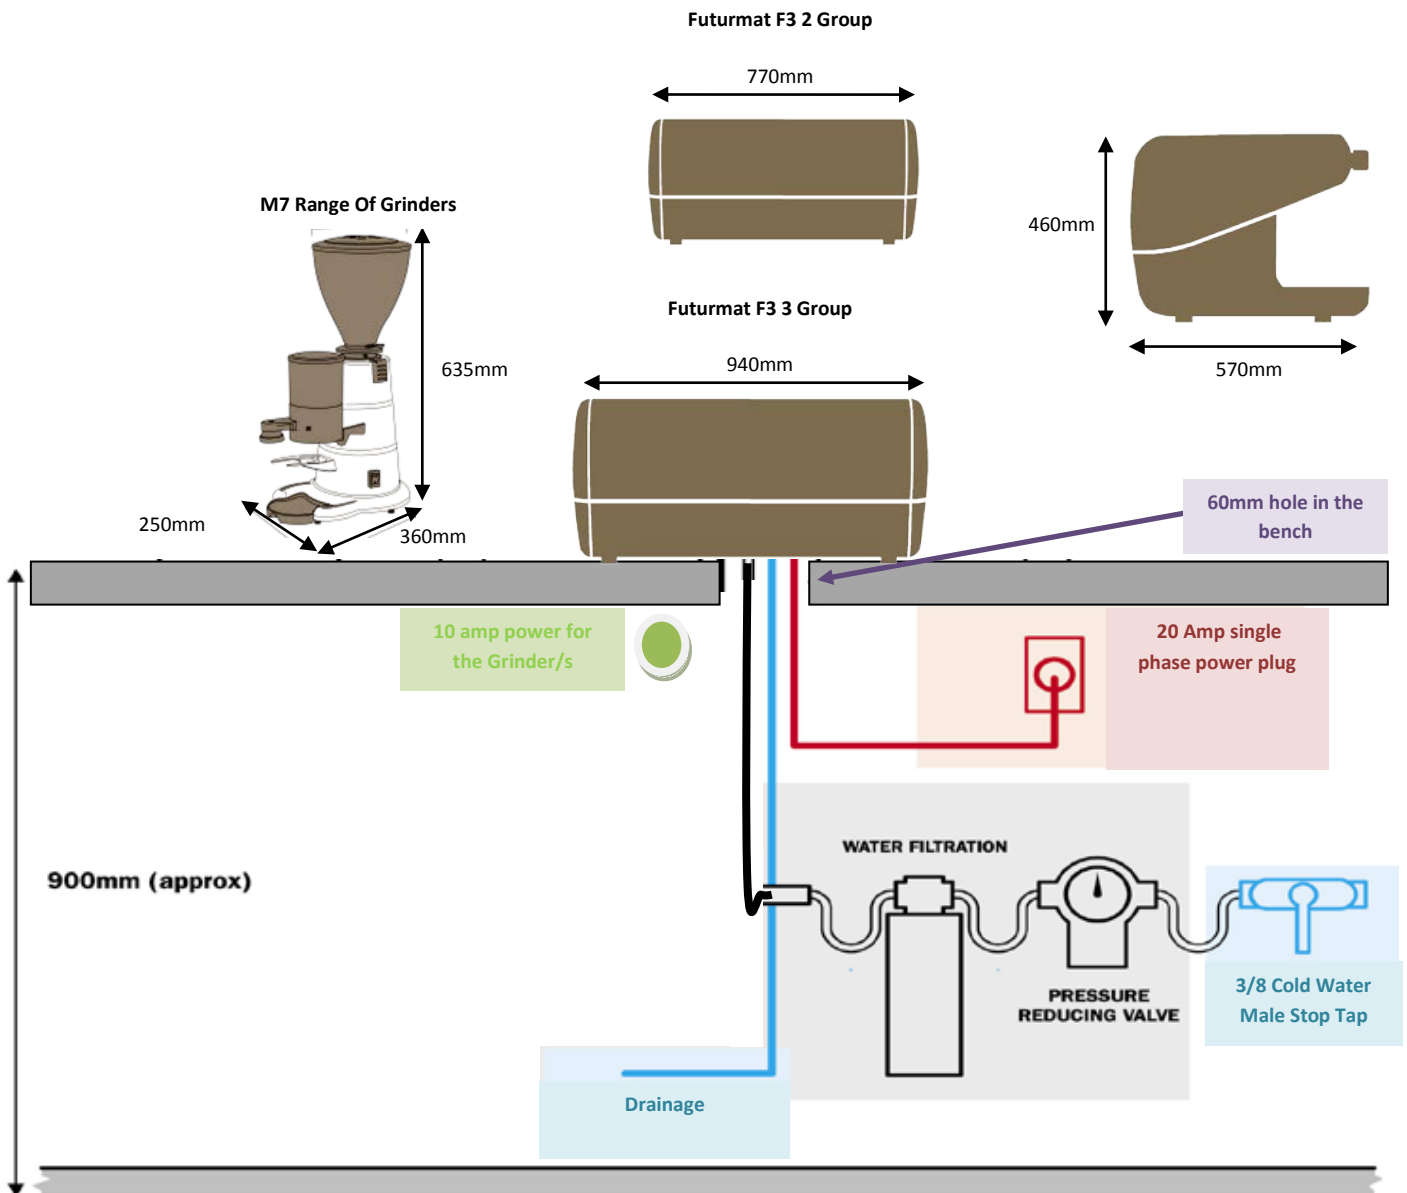

15 Amp single phase wall outlet



3/8 Cold Water Male stop tap



Drainage



20 Amp single phase wall outlet



20 Amp single phase wall outlet



FUTURMAT Site Ready Checklist for the F3



✓ Please complete form below. If cancellation occurs without 24-hours notice or a technician has to return due to site not being ready, additional service charges will apply. Please contact GCS if you have any queries 1300 552 883.
INSTALLATION WILL NOT TAKE PLACE UNTIL THIS CONFIRMATION FORM HAS BEEN EMAILED OR FAXED BACK TO GLOBAL COFFEE SOLUTIONS- email sales@globalcoffee.com.au or 02 4284 6099

Customer Name:

Store Address:

Bench Space for:

- Futurmat F3 3 Group -460h x 570d x 940w mm
- Futurmat F3 2 Group - 460h x 570d x 770w mm
- Macap M7 Range of grinder - 635h x 360d x 250w mm

- 3 Group F3 – 20 Amp single phase wall outlet within 1 mtr of machine
- 2 Group F3 – 15 Amp single phase wall outlet within 1 mtr of machine
- 10 Amp single phase wall outlet/s within 1 mtr of machine per grinder
- 3/8 Cold Water Male stop tap within 1 mtr of machine
- Drainage within 1 mtr of machine – open tundish or s bend
- 60mm hole in the bench where machine is located
- Internal cupboard holes drilled [if cabling requires travelling through]

Accessibility:

- Stairs – Yes/No – If yes how many:
- Parking available on site

Consumables Available at time of install – Yes/ No

Staff Must Be Available for training at completion of the installation – Yes/No

Additional Notes:

Store Owner's Name:

Signature:

Date:

By faxing back this Order Confirmation form the customer is confirming that there is sufficient power and space to install the machine. Should this not be the case, upon installation the customer will be charged for all service fees incurred.

